CET257 Enterprise Project: Assignment 2

Task B3: Report Evaluating Client Interactions

Team Speed (Team 6) · Lift Right: 360° Manual Handling Training Simulation

Client: Sulav G. Raj, Vantec

1. Overview

Over the project, Team Speed had six kinds of contact with our client, Sulav G. Raj, who also acted as our module tutor: an introductory email, a consultancy call, a requirement review, a prototype demonstration, follow-up emails, and a final client presentation. Table 1 summarises them. This report evaluates what worked and what did not, and recommends how we could have communicated better. The evidence (C1 to C11) is in the appendices.

No.	Date	Contact	Purpose and outcome	Evidence
1	16 July	Introductory email	Introduced the team and asked for a 15-to-20-minute call.	C1
2	16 or 18 July	Consultancy call (phone)	Introduced Lift Right. The client confirmed that current training is routine and easy to forget. A follow-up review was agreed.	C2, C3
3	10 August	Requirement review (Google Meet)	Walked through the six checkpoints, scoring and supervisor view. The client was largely satisfied and gave feedback on scope.	C4, C5
4	3 September	Prototype demonstration (in person)	Full team demonstrated navigation, the quiz sequence and live scoring. Positive response, with two small scope adjustments requested.	C6, C7, C8
5	12 September	Final thank-you email	Shared the live prototype link and thanked the client.	C9
6	Final session	Client presentation	Rated 4, 5, 5, 5 and 5 out of 5, with four improvement comments.	C10, C11

Table 1: Summary of client interactions

2. Best Aspects

- **The early introduction and call set the direction.** The client confirmed that posters and PDF inductions do not stick with staff. That gave the project a clear purpose, which shaped every later decision.
- **Meetings matched the project stages.** Discovery, requirement validation and demonstration each had a stated purpose, and the next meeting was booked before the previous one ended.
- **Follow-up was consistent.** We emailed after each contact, restating what we heard and what came next. This kept the relationship professional.
- **The in-person demonstration was the most productive.** The client reacted to a working build, not documents, and the later presentation rating of 24/25 reflected this.

3. Worst Aspects

- **Feedback was recorded without detail.** Our logs say "feedback on scope" and "two small scope adjustments" but do not name them. Only the replay feature (FR14) can be traced to a requirement, so we cannot show clearly how each comment was handled.
- **Records contained avoidable errors.** The call is logged on 16 July but the thank-you email is dated 18 July. The follow-up email is dated 11 August for a meeting held on 10 August. One email calls Thursday 3 September a "Tuesday". Some action dates were left as placeholders and client signature fields are blank. These errors weaken the evidence.
- **Contact was too infrequent and too late.** There were 24 days between the requirement review and the demonstration, and no meeting after the demo to confirm the adjustments. The most useful feedback (layout, varied scoring and engagement) came at the final presentation, when there was little time left to build it.
- **Too few of us spoke to the client.** The consultancy call was led by one person. The people building the system met the client only at the demonstration, so technical questions went unasked.
- **The client's dual role added ambiguity.** Because our client was also our tutor, it was sometimes hard to separate project advice from assessment expectations.

4. Evaluation of the Consultancy Session

The call had a clear purpose and the client spoke openly about his own experience, which confirmed our problem statement. However, it was short, and our records show no prepared list of questions. We did not record questions about the devices workers use, IT restrictions, the number of trainees, languages, accessibility, or how success would be measured. These gaps later surfaced as assumptions in our design, for example the choice of browser-only, client-side storage. The session confirmed the problem well but produced few concrete requirements.

5. Recommendations

- **Prepare:** send an agenda and question list (devices, users, constraints, success measures) at least 48 hours before each session.
- **Share the roles:** have two team members at every contact, one leading and one taking notes, and include a technical team member at the first consultancy session.
- **Keep a feedback register:** record each comment with an ID, the client's exact words, date, owner, linked requirement and status, and update it within 24 hours.
- **Confirm in writing:** email minutes within 24 hours and ask the client to confirm or correct them, instead of leaving blank signatures and placeholder dates.
- **Add checkpoints:** include a mid-build check around Week 6 and a short post-demo confirmation, so the final presentation holds no surprises.
- **Ask for feedback earlier:** book the presentation feedback session while there is still time to build the changes.
- **Agree boundaries:** at the start, agree how the client's advice differs from the marking criteria.

6. Conclusion

Our client interaction gave the project a clear purpose and a positive final response. It was weakest in preparation, record keeping and timing. Following the recommendations above would make each contact more useful and the evidence more reliable.

Appendix A: Evidence Index

The original documents are provided in the evidence folder, and the screenshots of emails are reproduced in Appendix C.


Ref	Evidence	File	Date
C1	Introductory email to the client	Evidence screenshot 1	16 July
C2	Meeting 1 log: introductory call	Meeting_1_Introductory_Call	16 July
C3	Thank-you email after the call	Evidence screenshot 2	18 July
C4	Meeting 2 log: requirement review	Meeting_2_Requirement_Review	10 August
C5	Email after the requirement review, proposing the demo	Evidence screenshot 3	11 August
C6	Email confirming the prototype demonstration	Evidence screenshot 4	1 September
C7	Meeting 3 log: prototype demonstration	Meeting_3_Prototype_Demonstration	3 September
C8	Thank-you email after the demonstration	Evidence screenshot 5	6 September
C9	Final thank-you email with the prototype link	Evidence screenshot 6	12 September
C10	Client presentation feedback form	feedback.pdf	Presentation day
C11	Presentation slides, plan and weekly minutes recording client contact	Lift_Right_Presentation.pptx, weekly minutes	Weeks 1 to 8

Appendix B: Meeting Minutes Summary

Meeting	Meeting 1: Introductory call	Meeting 2: Requirement review	Meeting 3: Prototype demonstration
Date and place	16 July, 10:30 AM, phone call	10 August, 11:00 AM, Google Meet	3 September, 8:30 AM, university classroom
Attendees	Shilu Chuke, Sulav G. Raj	Shilu Chuke, Swikriti Bashyal, Sulav G. Raj	All four team members, Sulav G. Raj
Purpose	Introduce Lift Right and hear the client's view of manual-handling training	Present early requirements and confirm the brief was understood	Demonstrate the working prototype
Client feedback	Existing training does not stick. Shared operational context.	Largely satisfied. Feedback on scope used to finalise requirements.	Positive response. Two small scope adjustments requested.
Agreed actions	Take feedback into requirements. Follow-up meeting booked.	Finalise Requirements. Continue the prototype. Schedule the demo.	Carry the two adjustments through and keep the project plan up to date.
Next meeting	10 August, Google Meet	3 September, in person	Not yet scheduled

Table B1: Summary of the three client meeting logs

Appendix C: Email Evidence

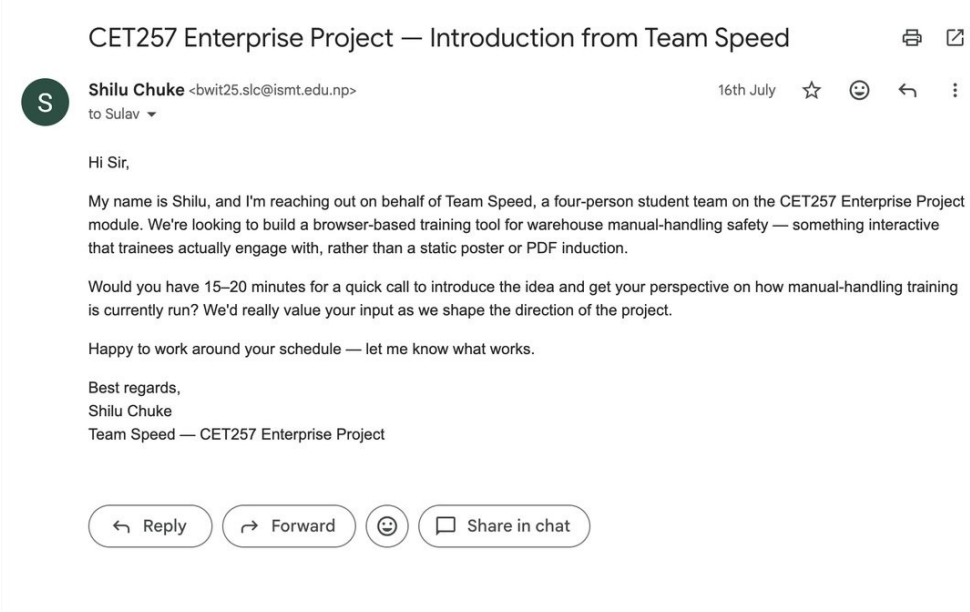

CET257 Enterprise Project — Introduction from Team Speed

Shilu Chuke <bwit25.slc@ismt.edu.np> 16th July
to Sulav

Hi Sir,

My name is Shilu, and I'm reaching out on behalf of Team Speed, a four-person student team on the CET257 Enterprise Project module. We're looking to build a browser-based training tool for warehouse manual-handling safety — something interactive that trainees actually engage with, rather than a static poster or PDF induction.


Would you have 15–20 minutes for a quick call to introduce the idea and get your perspective on how manual-handling training is currently run? We'd really value your input as we shape the direction of the project.

Happy to work around your schedule — let me know what works.

Best regards,
Shilu Chuke
Team Speed — CET257 Enterprise Project

Reply Forward Share in chat

C1: Introductory email to the client, 16 July

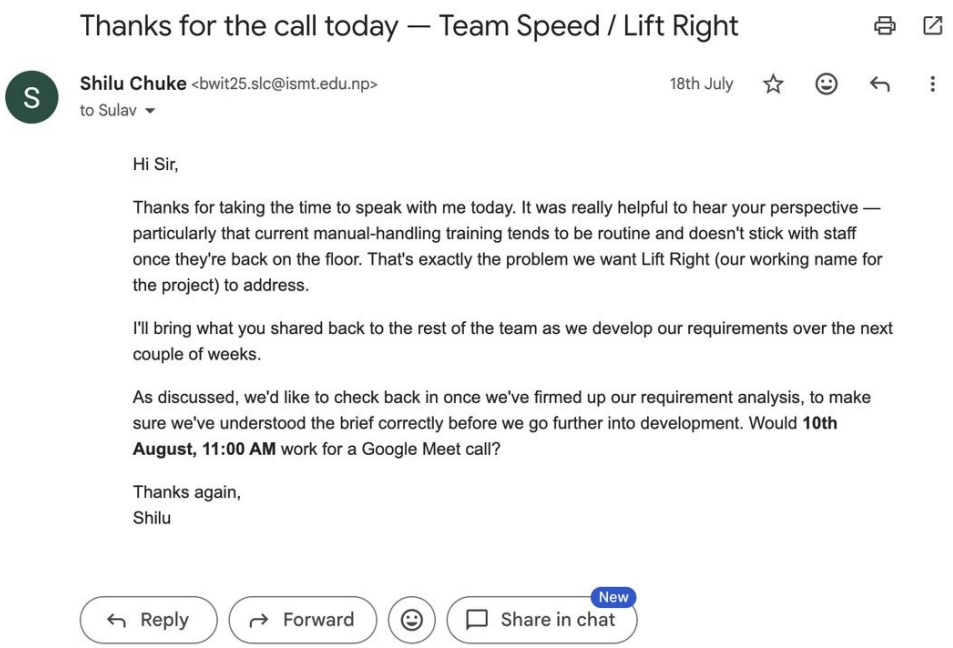

Thanks for the call today — Team Speed / Lift Right

Shilu Chuke <bwit25.slc@ismt.edu.np> 18th July
to Sulav

Hi Sir,

Thanks for taking the time to speak with me today. It was really helpful to hear your perspective — particularly that current manual-handling training tends to be routine and doesn't stick with staff once they're back on the floor. That's exactly the problem we want Lift Right (our working name for the project) to address.

I'll bring what you shared back to the rest of the team as we develop our requirements over the next couple of weeks.

As discussed, we'd like to check back in once we've firmed up our requirement analysis, to make sure we've understood the brief correctly before we go further into development. Would **10th August, 11:00 AM** work for a Google Meet call?

Thanks again,
Shilu

Reply Forward Share in chat New

C3: Thank-you email after the call, 18 July

Thanks for the requirement review — next step: prototype demo

Shilu Chuke <bwit25.slc@ismt.edu.np> 11th August
to Sulav

Hi Sir,

Thanks for reviewing our requirement thinking with us today — glad to hear you're largely happy with the direction. We've noted your feedback on scope and will be finalising our Requirements document with that in mind.

The team is now moving into prototype development: the six-checkpoint manual-handling sequence, scoring, and the supervisor-facing dashboard we talked through.

We'd love to show you the working build once it's ready. Would **3rd September, 8:30 AM, in person** suit you for a prototype demonstration?

Best,
Shilu

Reply Forward Share in chat (New)

C5: Email after the requirement review, 11 August

Confirming prototype demo — 3rd September, 8:30 AM

Shilu Chuke <bwit25.slc@ismt.edu.np> 1st September
to Sulav

Hi Sir,


Just confirming we're on for **Tuesday 3rd September at 8:30 AM**. The full team will be there to walk you through the working prototype — navigating the warehouse zones, the checkpoint/quiz sequence, and the live scoring dashboard.

Looking forward to getting your feedback on the build.

See you then,
Shilu

Reply Forward Share in chat (New)

C6: Email confirming the prototype demonstration, 1 September

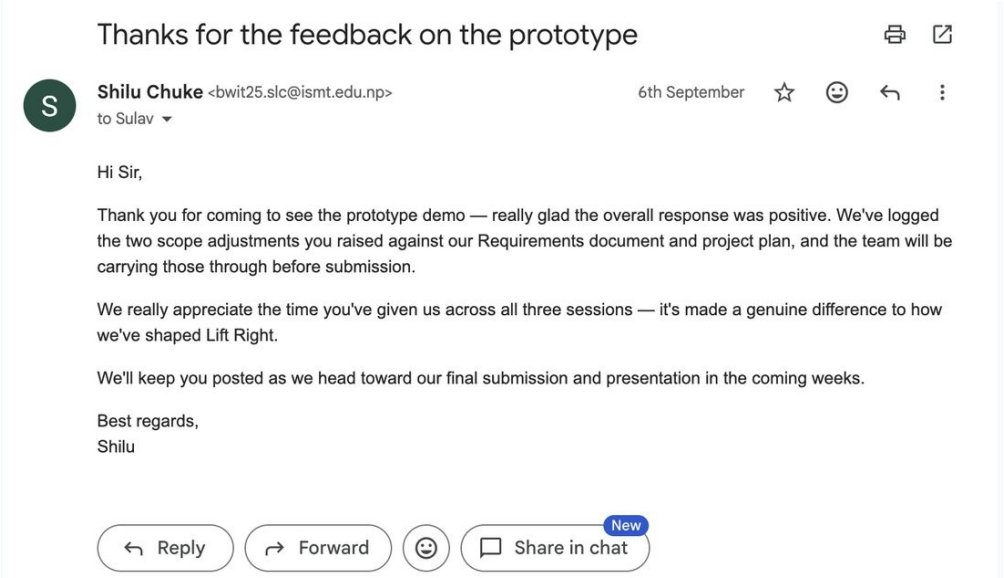

Thanks for the feedback on the prototype

Shilu Chuke <bwit25.slc@ismt.edu.np> 6th September

to Sulav

Hi Sir,

Thank you for coming to see the prototype demo — really glad the overall response was positive. We've logged the two scope adjustments you raised against our Requirements document and project plan, and the team will be carrying those through before submission.


We really appreciate the time you've given us across all three sessions — it's made a genuine difference to how we've shaped Lift Right.

We'll keep you posted as we head toward our final submission and presentation in the coming weeks.

Best regards,
Shilu

Reply Forward Share in chat New

C8: Thank-you email after the demonstration, 6 September

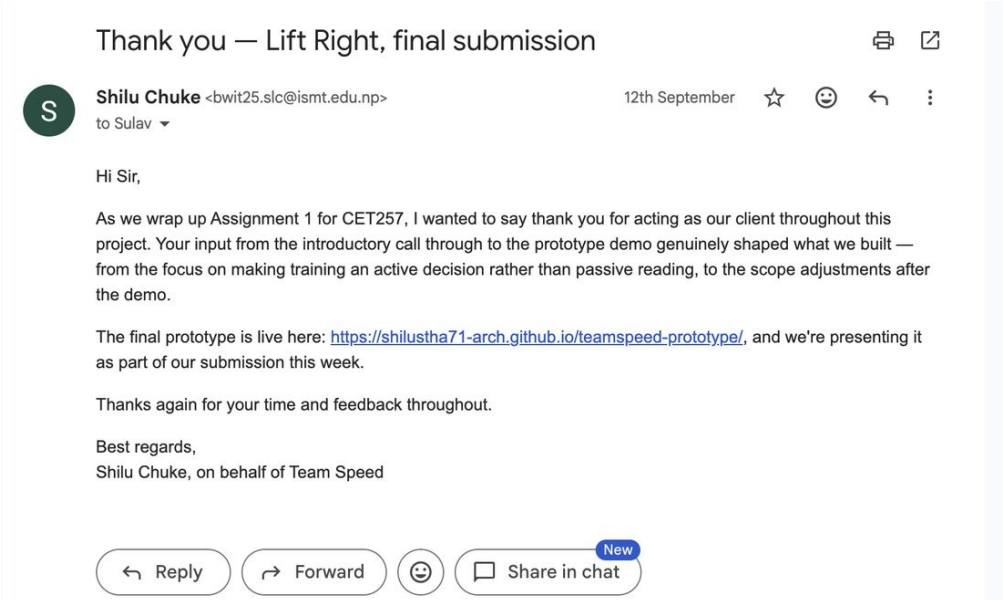

Thank you — Lift Right, final submission

Shilu Chuke <bwit25.slc@ismt.edu.np> 12th September

to Sulav

Hi Sir,

As we wrap up Assignment 1 for CET257, I wanted to say thank you for acting as our client throughout this project. Your input from the introductory call through to the prototype demo genuinely shaped what we built — from the focus on making training an active decision rather than passive reading, to the scope adjustments after the demo.

The final prototype is live here: https://shilustha71-arch.github.io/teamspeed-prototype/, and we're presenting it as part of our submission this week.

Thanks again for your time and feedback throughout.


Best regards,
Shilu Chuke, on behalf of Team Speed

Reply Forward Share in chat New

C9: Final thank-you email, 12 September

Appendix D: Client Presentation Feedback

The client rated our presentation 4, 5, 5, 5 and 5 out of 5, left four comments and signed the form (page 2). The team intended to update the layout for selecting options, give the point system more variation, add more ways to earn points, and make the experience more engaging and interactive.

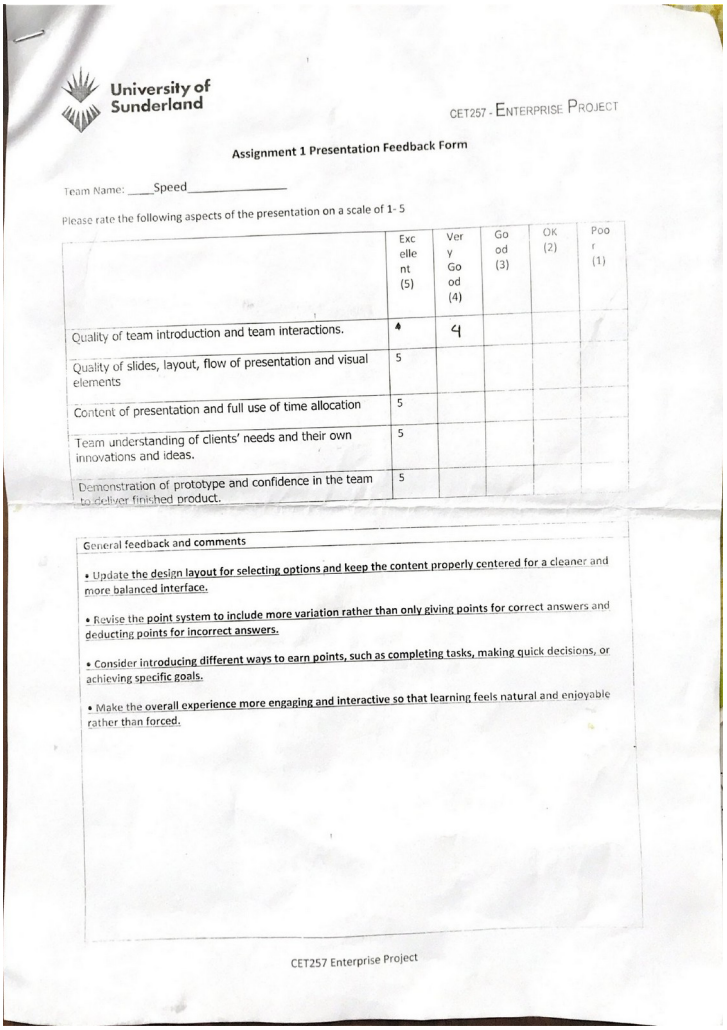

University of Sunderland

CET257 - ENTERPRISE PROJECT

Assignment 1 Presentation Feedback Form

Team Name: ____Speed_____

Please rate the following aspects of the presentation on a scale of 1- 5


	Excellent (5)	Very Good (4)	Good (3)	OK (2)	Poor (1)
Quality of team introduction and team interactions.	4	4			
Quality of slides, layout, flow of presentation and visual elements	5				
Content of presentation and full use of time allocation	5				
Team understanding of clients' needs and their own innovations and ideas.	5				
Demonstration of prototype and confidence in the team to deliver finished product.	5				

General feedback and comments

- Update the design layout for selecting options and keep the content properly centered for a cleaner and more balanced interface.
- Revise the point system to include more variation rather than only giving points for correct answers and deducting points for incorrect answers.
- Consider introducing different ways to earn points, such as completing tasks, making quick decisions, or achieving specific goals.
- Make the overall experience more engaging and interactive so that learning feels natural and enjoyable rather than forced.

CET257 Enterprise Project

C10: Client presentation feedback form (page 1)



Client Signature: .....

C10: Client signature on the feedback form (page 2)
